


ID	Task Name	Duration	Start	Finish	May								
					M	F	T	S	W	S	T	M	
1	<b>St Michael Parish Hall</b>	<b>55 days</b>	<b>Mon 3/24/14</b>	<b>Fri 6/6/14</b>									
2	<b>Preconstruction</b>	<b>15 days</b>	<b>Mon 3/24/14</b>	<b>Fri 4/11/14</b>									
3	Subcontractor Selection	5 days	Mon 3/24/14	Fri 3/28/14									
4	Contract	1 day	Fri 3/28/14	Fri 3/28/14									
5	Submittals	10 days	Mon 3/31/14	Fri 4/11/14									
6	Construction-Permit-Dust-	1 day	Fri 4/4/14	Fri 4/4/14									
7	<b>Construction</b>	<b>47 days</b>	<b>Thu 4/3/14</b>	<b>Fri 6/6/14</b>									
9	Johnson Water Submittal Review	6 days	Thu 4/3/14	Thu 4/10/14									
8	Mobilize-Hydrant meter-Inspector	1 day	Mon 4/7/14	Mon 4/7/14									
10	Survey Utilities	1 day	Mon 4/7/14	Mon 4/7/14									
11	Sawcut asphalt	1 day	Fri 4/11/14	Fri 4/11/14									
12	Traffic Control #1-one lane @ Day	1 day	Mon 4/14/14	Mon 4/14/14									
13	Excavate Install sewer line	8 days	Mon 4/14/14	Wed 4/23/14									
14	Excavate Install water lines	2 days	Thu 4/24/14	Fri 4/25/14									
15	Survey for curb, Road grade	2 days	Fri 4/25/14	Mon 4/28/14									
16	Traffic Control #2- Detour around	1 day	Mon 4/28/14	Mon 4/28/14									
17	Grade / remove spoils	6 days	Mon 4/28/14	Mon 5/5/14									
19	Install A/B grade	5 days	Tue 5/6/14	Mon 5/12/14									
20	Traffic Control #3 working room	1 day	Tue 5/13/14	Tue 5/13/14									
18	Install Curbs-Sidewalk-Drives	10 days	Tue 5/13/14	Mon 5/26/14									
21	Fine Grade / Install Pavement	4 days	Tue 5/27/14	Fri 5/30/14									
22	Obliterate street markings	1 day	Mon 6/2/14	Mon 6/2/14									
23	City Finals, final clean up- punch	5 days	Mon 6/2/14	Fri 6/6/14									

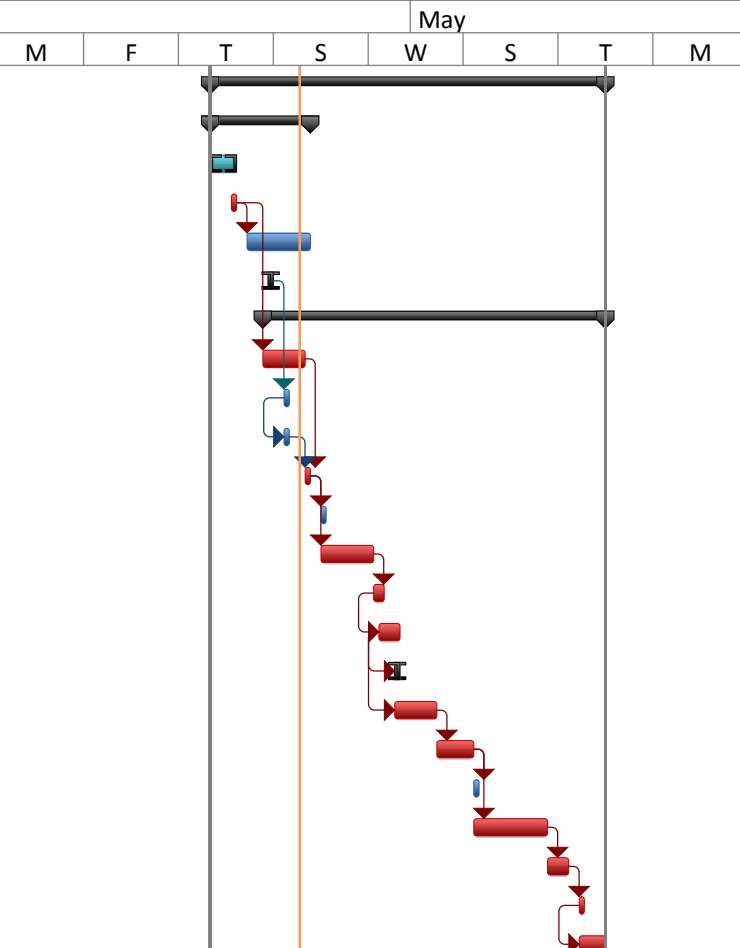

Project: St Michaels Parish baselin Date: Thu 4/10/14	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Critical	
	Project Summary		Duration-only		Critical Split	
	External Tasks		Manual Summary Rollup		Progress	
	External Milestone		Manual Summary			
